



Construction of the West 132nd Avenue and Zuni Street Storm Drainage Improvements Project, Neighborhood Entry Sign, and Median Landscaping

PROGRESS REPORT

January 24, 2014

Questions?

Contacts at the City and County of Broomfield:

CIP Project Manager:
Kathryn Bergh
303.464.5802
kbergh@broomfield.org

CIP Field Manager:
Jack Haines
303.901.0404
jhaines@broomfield.org

Contractor:
Randy Kiser,
Project Manager
New Design Construction Co.
303.286.8500
bohlemeier@
newdesignconstruction.com

Visit the City & County of Broomfield's website for information on other projects...

www.broomfield.org

Thank you for your patience during construction!

Introduction

The Broomfield City Council approved a construction agreement with New Design Construction to construct the West 132nd Avenue and Zuni Street Storm Drainage Improvements Project. The project involves replacement of the grated drain structure with local inlets and subsurface storm sewer draining to Alexx and Michael's Pond. The new drainage configuration will improve public safety and surface drivability at the intersection, while more effectively capturing storm runoff and reducing future annual maintenance.

A vicinity map of the proposed project location is shown below.



Construction was originally scheduled to begin in November 2013. Work was delayed due to a utility conflict and relocation and the holiday season. New Design Construction is scheduled to mobilize the week of February 3rd, weather depending.

This summer landscaping enhancement and a neighborhood entry sign are proposed for construction in the West 132nd Avenue median. These improvements are identified in the Westlake Neighborhood Plan, which was developed through a series of neighborhood meetings and approved by City Council in May 2009. On the reverse side of this newsletter is a concept plan for the sign. The new landscaping will be similar to the Westlake Drive median at Lowell Boulevard and will include five trees.

Anticipated Project Construction Schedule – Storm Drainage Improvements

South Side of West 132nd Avenue Median:

- Sidewalk, Curb and Gutter, Drainage Grate, and Inlet Removal: February 10–14
- Storm Pipe, Inlet, Drain Pan, and Riprap Construction: February 18–March 6
- Subgrade Preparation and Asphalt Paving: March 5–13

North Side of West 132nd Avenue Median:

- Sidewalk, Curb and Gutter, Drainage Grate, and Inlet Removal: March 17–19
- Storm Pipe, and Inlet Construction: March 13–28
- Subgrade Preparation and Asphalt Paving: April 4–9


Please keep in mind weather may impact the construction schedule and sequencing.

Traffic

During construction, lane shifts and lane closures will impact vehicle, bicycle, and pedestrian traffic at the intersection of West 132nd Avenue and Zuni Street.

Construction Hours

Work hours will be limited to 7:00 a.m. to 7:00 p.m., Monday through Friday, and occasionally on Saturdays from 9:00 a.m. to 3:30 p.m. Residents will be notified if work hours change.

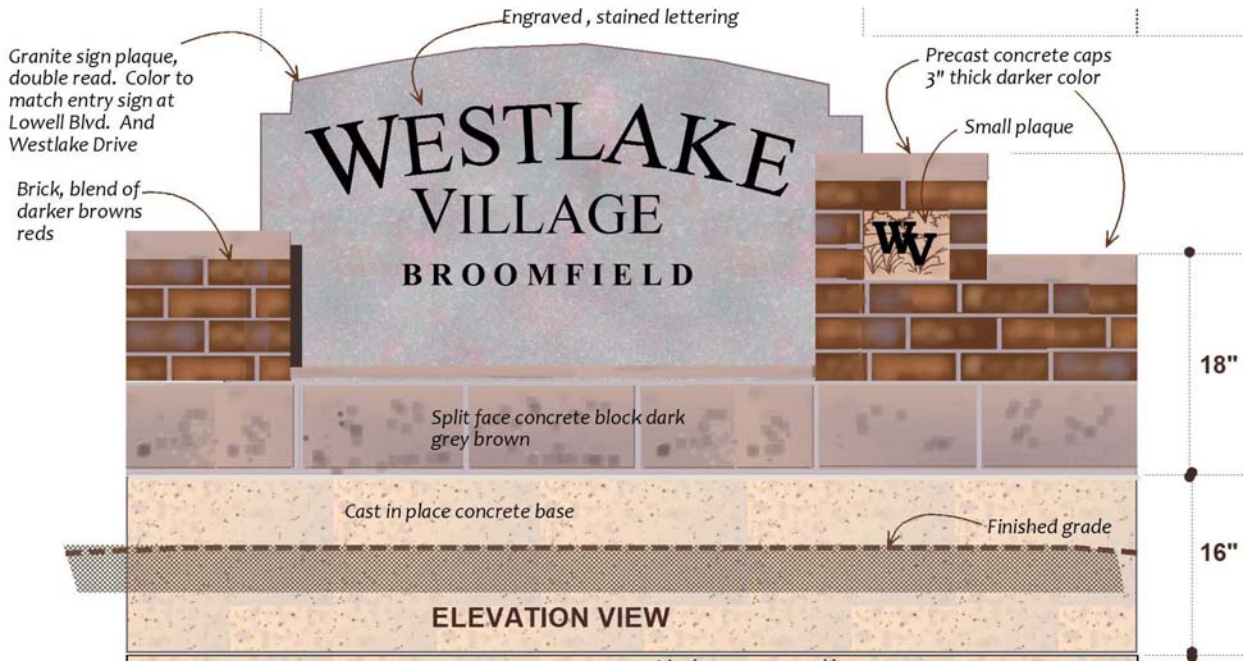

Concept Plan for Neighborhood Entry Sign in West 132nd Avenue Median at Zuni Street
(Spring 2014 Construction)
